



Southwest Michigan Planning Commission

376 West Main Street, Suite 130 • Benton Harbor, MI 49022-3651

TWIN CITIES AREA TRANSPORTATION STUDY TECHNICAL ADVISORY and POLICY COMMITTEES **COMBINED** MEETING

FOR FURTHER INFORMATION CONTACT:

Kim Gallagher, *Transportation Planner*

(269) 925-1137 x 1518

Brandon Kovnat, *Transportation Planner*

(269) 925-1137 x1524

DATE: Monday, June 19, 2017

TIME: 9:30AM

PLACE: Kinexus (Michigan Works!) Anchor Rooms A + B,
499 W Main St, Benton Harbor, MI 49022

AGENDA

1. Call to Order / Introductions
2. Changes to the Agenda
3. Public Comment
4. Approve Minutes from the May 15, 2017 Meeting (*Enclosed*) **Action**
5. Staff Report
 - Napier Corridor Study
6. Community Land Use and Zoning Member Updates
7. Public Transit
 - SWMPC Transit Updates – (Countywide Transit Study) – Kim Gallagher
 - Twin Cities Area Transportation Authority – Bill Purvis
8. Air Port Updates – Vince Des Jardins
9. Agency Project Status (*Enclosed*)
 - Berrien County Road Commission
 - Village of Stevensville
 - City of Benton Harbor
 - City of St. Joseph
 - MDOT
10. Old Business
 - None
11. New Business
 - Replacement of the Policy Committee chair
 - Amendment Requests
 - City of Benton Harbor CMAQ Project (*Enclosed*) **Action**
 - Public Participation Plan Discussion and Approval **Action**
 - State and Federal Updates
12. Privilege of the Floor
13. Adjournment
 - The next TwinCATS meeting is scheduled for: **Monday, July 17, 2017 @ 9:30 am.**

**TWIN CITIES AREA TRANSPORTATION STUDY
TAC and Policy Committee Combined Minutes**

May 15, 2017 9:30 A.M.
Kinexus, Anchor Rooms A&B

Present		Committee Representing	
Name	Representing	TAC	Policy
Carolyn Fowler	Benton Charter Township		x
Kelli Nelson	Benton Charter Township	x	
Bill Chickering	Berrien County Commission		x
Evan Smith	Berrien County Community Development	x	
Bill Hodge	Berrien County Planning Commission		x
Brian Berndt	Berrien County Road Commission	x	
Chris Cook	City of Benton Harbor	x	
Tim Zebell	City of St. Joseph	x	
John Hodgson	City of St. Joseph		x
Stacey Stephens	Cornerstone Alliance	x	x
Dick Stauffer	Lincoln Charter Township		x
Jonathon Smith	MDOT Coloma TSC	x	x
Jason Latham**	MDOT Southwest region	x	x
Jim Sturdevant	MDOT Statewide Planning	x	X
Scott Weber	Northwestern Indian Regional Planning Commission*	x	x
Steve Tilly	Royalton Township		x
Jonathan Fisk**	St. Joseph Charter Township	x	
Eric Lester			
Brandon Kovnat	SWMPC	Staff	
Kim Gallagher	SWMPC	Staff	
Absent		TAC	POL
Tim Lynch	Berrien County Road Commission		x
Darin Watson	City of Benton Harbor		x
Juan Ganum	City of Bridgman	x	x
Terezie Harazinova	Disability Network Southwest Michigan	x	
Andy Pickard	Federal Highway Administration*	x	x
Kishina Welch	Federal Transit Administration*	x	x
Deb Kavenah	Hagar Township		
Gloria Payne	Lake Charter Township	x	x
Terrie Smith	Lincoln Charter Township	x	
Fred Featherly	MDOT Passenger Division	x	
Denise Smith	MDOT Southwest Michigan	x	x

Absent		TAC	POL
Katie Beck	MDOT SUTA*	x	
David Chandler	Sodus Township	x	x
Vince Desjardins	Southwest Michigan Regional Airport	x	x
Denise Cook	St. Joseph Charter Township		x
Ron Griffin**	St. Joseph Charter Township		
Roger Seeley	St. Joseph Charter Township	x	
Bill Purvis	TCATA	x	x
John Olson	Village of Stevensville	x	x

*Non-Voting **Alternate Member

1. Call to Order / Introductions

Meeting called to order by Brian Berndt at 9:30 AM

2. Changes to the Agenda

None

3. Public Comment

None

4. Approve Minutes from the April 17, 2017 Meeting *(Enclosed)* Action

Motion to approve the minutes from the April 17, 2017 Meeting as written by Steve Tilley, second Dick Stauffer. **Motion Approved**

5. Staff Report

Kim Gallagher gave an update on the Napier Corridor study. The Request of Proposals (RFP) was sent out last Tuesday May 9

6. Community Land Use and Zoning Member Updates

Jonathon Fisk said that St. Joseph Charter Township was holding a public hearing on their new Master plan on June 13 at 6:30 PM.

7. Public Transit

Kim Gallagher gave an update on the Connect Berrien
Update on ridership figures for TCATA

8. Air Port Updates – Vince Des Jardins

None

9. Agency Project Status

Brian Berndt gave an update on Berrien County Road Commission Projects:

- River Road was let on 2/3/2017; Construction began on 4/17/17.
- John Beers road was Let on 4/7/17 Construction will begin in July
- Hilltop Road was let on 2/3/17 Construction began 3/20/17

MDOT office of Rail

- Hilltop Road Rail Crossing was obligated on 3/3/17. Construction began 5/1/17

Chris Cook gave the update on behalf of the Village of Stevensville and for the city of Benton Harbor

- The Red Arrow & John Beers Road Intersection project was let on 3/3/17. Construction awaiting MDOT authorization; estimated for June.
- Colfax South had Grade Inspection meeting on 5/1/17. Estimated to be obligated in July and constructed in September.

Tim Zebell gave the first update for the 2018 Wallace Avenue reconstruction.

- Funding Resolution signed 4/24/17. The RFP for engineering will be sent 5/19/17

Jonathon Smith gave updates for MDOT projects

- I-196 Overlay: Contract authorized. Kickoff meeting was 5/11/17
- M-139: As needed consultant for engineering work began in May
- M-63 Overlay: Let 4/7/17 and construction to begin in June
- M-63 Crack Fill: Let in February and construction scheduled to begin 5/17/17.
- US-31 Longitudinal Joint repair: Project let in January and construction scheduled to begin 6/26/17

Jonathon said that public outreach for the I-94 EPE would begin in the next couple of weeks. He said that MDO was working on traffic signal projects that occur in the TwinCATS area but are part of a general program account (GPA) and are not listed by individual location on the TIP.

10. Old Business

None

11. New Business

TCATA needs to correct their 2017 Bus Purchase using federal 5339 funds. The TIP had the total project costs listed as \$85,498. Bill Purvis said that this was actually supposed to be the federal cost. The total cost would be \$106,893. Because this is an increase of 25%, it has to be committee approved.

	Currently in TIP	Amendment
Federal 5339	\$68,388	\$85,498
State CTF	\$17,100	\$21,375
Total	\$85,498	\$106,893

Motion for the Technical Advisory Committee to recommend approval of an amendment to the 2017-2020 Transportation Improvement Program to correct the funds entered for TCATA's FY 2017 Bus Purchase using federal 5339 funds, by Tim Zebell, second by Chris Cook. **Motion Approved.**

Motion for the Policy Committee to approve an amendment to the 2017-2020 Transportation Improvement Program to correct the funds entered for TCATA's FY 2017 Bus Purchase using federal 5339 funds, by Dick Stauffer, second by Jim Sturdevant. **Motion Approved.**

MDOT is proposing to increase the budget for their fy2017 I-94 Subsurface Repair.

	Currently in TIP	Amendment
SUB Phase		
State M	\$39,259	\$69,259
CON Phase		
Federal IM	\$472,075	\$782,574
State M match	\$52,454	\$86,953
Subtotal for CON Phase	\$524,529	\$869,527
Total Project Cost	\$563,788	\$938,786

Motion for the Technical Advisory Committee to recommend approval of an amendment to the 2017-2020 Transportation Improvement Program to increase the funding for MDOT's FY 2017 I-94 Subsurface Repair, by Chris Cook second by Jason Latham. **Motion Approved.**

Motion for the Policy Committee to approve an amendment to the 2017-2020 Transportation Improvement Program to increase the funding for MDOT's FY 2017 I-94 Subsurface Repair, by Steve Tilley second by Carolyn Fowler. **Motion Approved.**

There was a brief discussion of The 2018 Unified Work Program (UWP). Scott Weber said that the UWP had the Northwest Indiana Regional Planning Commission, which should have been the Northwestern Indiana Regional Planning Commission.

Jim Sturdevant said that once the MPO committees approved the UWP it would still be reviewed by MDOT and the FHWA. They could ask for changes. Thus, any approval should be conditional to allow for required changes. This would allow for minor changes before official FHWA approval without requiring an amendment process. Brandon said that he would inform the MPO of any changes between the current draft and the final version.

Motion for the Technical Advisory Committee to recommend approval of the FUY 2018 Unified Work Program, with any subsequent changes required by MDOT or FHAWA, by Chris Cook, Second by Tim Zebell. **Motion Approved.**

Motion for the Policy Committee to approve the FUY 2018 Unified Work Program, with any subsequent changes required by MDOT or FHAWA, by Steve Tilley, Second by Bill Hodge.

Motion Approved.

State and federal Updates

Jim Sturdevant said that MDOT was finishing the base year travel demand model and would be coming out with future forecast data shortly.

12. Privilege of the Floor

Tim Zebell said that Ship Street was still in desperate need for repairs.

13. Adjournment

Meeting adjourned at 10:40 am

Minutes Compiled by: Brandon Kovnat, SWMPC Associate Planner

Transportation Improvement Program for the Twin Cities Area Transportation Study FY 2017 Projects

FY 2017 STP Urban

Responsible Agency	Project Name	MDOT Job #	Project Limits	Project Length (miles)	Improvement Type	Federal Cost	Local Cost	Total Phase Cost
Berrien County Road Commission	Hilltop Road	120848	BL-94 to M-63	1.0	Restore & rehabilitate	\$565,000	\$125,289	\$690,289
Berrien County Road Commission	John Beers Road	120849	0.32 miles east of Hollywood Road to 0.51 miles West	0.83	Resurface	\$192,163	\$46,600	\$238,763
City of Benton Harbor	Colfax South Resurfacing	130791	May to Emery	0.25	Resurface	\$87,000	\$42,000	\$228,000
FY 2017 STP-Urban Total						\$844,163	\$171,899	\$1,016,052

FY 2017 Bridge Replacement - STP Funded but Not Part of the MPO's Allocation

Responsible Agency	Project Name	MDOT Job #	Project Limits	Improvement Type	Federal Cost	State Cost	Local Cost	Total Phase Cost
Berrien County Road Commission	River Road	126674	Over Pipestone Creek	Bridge replacement	\$864,00	\$162,000	\$54,000	\$1,080,000

FY 2017 MDOT Projects

Project Name	MDOT Job #	Project Limits	Project Length (miles)	Improvement Type	Phase	Federal Cost	State Cost	Total Phase Cost
M-139 Passing Flare	127448	M-139 between Tanglewood and Anna	0.71	Traffic ops/safety	ROW	\$4,093	\$907	\$5,000
M-139 Passing Flare	127448	M-139 between Tanglewood and Anna	0.71	Traffic ops/safety	PE	\$53,096	\$11,774	\$64,870
I-196 Overlay	118792	I-94 to 0.5 miles South of M-63 (Exit 7)	8.09	Restore & rehabilitate	ROW	\$22,500	\$2,500	\$25,000
US-31 Longitudinal Joint repair	128742	Temp End Freeway to S JCT I-94	1.90	Resurface	CON	\$234,036	\$51,897	\$285,933
M-63 Crack Fill	128736	M-63 from I-94 to Midway	2.20	Restore & rehabilitate	CON	\$28,412	\$6,300	\$34,712
M-63 Overlay	127563	on M-63 from Winchester to I-94 BL	1.13	Resurface	CON	\$80,525	\$17,856	\$98,381
I-94 Road and Bridge Scoping	132824	0.5 miles west of I94 BL(exit 23) to the St. Joseph River	3.50	Miscellaneous	EPE	\$4,093	\$400,000	\$400,000
I-94 Substructure Repair	200006	Over I-94 BL (Lakeshore Dr.)		Bridge restore & rehabilitate	SUB	\$53,096	\$39,259	\$39,259
I-94 Substructure Repair	200006	Over I-94 BL (Lakeshore Dr.)		Bridge restore & rehabilitate	CON	\$22,500	\$52,454	\$524,529

FY 2017 TCATA Transit Projects

Project Name	Fund Source	Federal Cost	State Cost	Local Cost	Total Cost
Regular Operating Expenses	5307	\$777,380	\$658,744	\$406,000	\$1,842,124
Bus Purchase	5307	\$205,194	\$51,300		\$256,494
Bus Purchase	5307	\$27,145	\$6,787		\$33,932
Mobility Manager	5310	\$60,000	\$15,000		\$75,000
Bus Purchase	5339	\$16,449	\$4,111		\$20,560
Replace One Bus	5339	\$68,398	\$17,100		\$85,498
Bus Purchase	CM	\$230,000	\$57,500		\$287,500
JARC			\$386,040		\$386,040
Bus Purchase	5307	\$68,398	\$17,100		\$85,498
Phone System	5307	\$7,200	\$1,800		\$9,000

FY 2017 Other Funding Sources

Responsible Agency	Project Name	MDOT Job #	Project Limits	Fund Source	Federal/State Cost	Local Cost	Total Phase Cost
Village of Stevensville	Red Arrow Highway and John Beers Road Intersection Improvements	130877	400 ft. south of John Beers Rd to 400 ft. North of John Beers Rd.	HSIP	\$355,505	\$39,501	\$395,005
Berrien County Road Commission	Territorial Road Culvert	131453	North Branch Road to Millburg Drive	RTF	\$709,167	\$329,548	\$1,038,715
Berrien County Road Commission	Hilltop Road Crossing Surface Replacement	200245	Hilltop Road, Rail Crossing	State Rail Funds	\$37,463	\$24,976	\$62,439
Berrien County Road Commission	Upgrading Guardrails on Various Primary Roads	130875	Broadway from Napier Ave to City of Benton Harbor Limits	HSIP	\$9,000	\$1,000	\$10,000
SWMPC	Rideshare	124467	Countywide	CMG	\$12,000		\$12,000

2018 STBG Urban

Responsible Agency	Project Name	MDOT Job #	Project Limits	Project Length (miles)	Improvement Type	Federal Cost	Local Cost	Total Phase Cost
Berrien county road Commission	Nickerson Avenue	130797	M-139 to 700 feet East of Woodley	0.64	Resurface	\$143,000	\$32,000	\$175,000
Berrien County Road Commission	Shawnee Road	130793	Jericho Road to Date Road	0.50	Reconstruct	\$ 268,925	\$184,075	\$453,000
City of St. Joseph	Wallace Avenue	133290	Lakeshore Drive to Lakeview Ave.	0.25	Reconstruct	\$460,000	\$1,000,000	\$1,460,000
FY 2018 STP-Urban Total						\$871,925	\$ 1,216,075	\$2,088,000

FY 2018 MDOT Projects

Project Name	MDOT Job #	Project Limits	Project Length (miles)	Improvement Type	Phase	Federal Cost	State Cost	Total Phase Cost
M-63 Bridge Replacement	115754	on M-63 over I-196		Bridge Replacement	CON	\$4,135,701	\$459,522	\$4,595,223
I-94 WB Overlay	128907	on I-94 from E of I-196 to W of M-140	5.60	Resurface	PE	\$195,197	\$ 21,689	\$216,886
I-196 Overlay	118792	I-94 to 0.5 miles South of M-63 (Exit 7)	8.09	Restore & rehabilitate	CON	\$15,840,000	\$1,760,000	\$17,600,000
EB I-94 Interchange	130008	From Britain Avenue to I-196	3.87	New route/structure (capacity increase)	PE	\$963,579	\$213,671	\$117,7250
					SUB	\$1,491,922	\$330,828	\$182,2750
Napier Avenue Carpool Lot	116509	At Napier Avenue and US-31		Roadside facility	CON	\$ 69,573	\$15,427	\$85,000

FY 2018 TCATA Transit Projects

Project Name	Fund Source	Federal Cost	State Cost	Local Cost	Total Cost
Regular Operating Expenses	5307	813836	726370	356000	1896206
Mobility Manager	5310	60000	15000		\$75,000
Facilities Improvement	5339	80000	20000		\$100,000
JARC			397347	33000	430347

FY 2017 Other Funding Sources

Responsible Agency	Project Name	MDOT Job #	Project Limits	Fund Source	Federal/State Cost	State Cost	Total Phase Cost
Berrien County Road Commission	Red Arrow Highway	129834	Bridgman city limits to 0.8 mi south	RTF	\$449,334	\$258,769	\$708,103
SWMPC	Rideshare		Countywide	CMAQ	\$12,000	-	\$12,000



Southwest Michigan Planning Commission

376 West Main Street, Suite 130 • Benton Harbor, MI 49022-3651

Project Update Sheet

Project Name:	Hilltop Road
Fiscal Year of award:	2017
Responsible Agency:	Berrien County Road Commission
MDOT Job Number:	120848
Project Limits:	M-63 to BL-94
Project Length:	1.0 miles
Location:	St. Joseph charter Township
Work Type:	Resurface
Phase:	CON

Project Description: Mill and Fill. ADA sidewalk upgrades and construction, depending on budget. Water main replacement

	Amount	Source
Federal	\$652,000	STP-Urban
State	-	-
Local	\$145,000	Berrien County & St Joseph
Total	\$797,000	

Activity	Estimated Date	Actual Date
Resolution of Support for Local Match Submitted to SMWPC		
Project Application Submitted to MOT		
Grade Inspection Package Submitted to MDOT		
Grade Inspection Meeting Scheduled		10/25/2016
Final Plan and Estimate to MDOT		12/2/2016
Project Obligated		
Project Letting	02/03/17	02/03/2017
Construction Start	3/20/17	3/20/17
Project Completion	7/14/17	

Project is: ☒ On Schedule ☐ Behind Schedule; Explain:

Date: 6/9/2017

Name: Brian Berndt

Southwest Michigan Planning Commission

376 West Main Street, Suite 130 • Benton Harbor, MI 49022-3651

Project Update Sheet

Project Name:	John Beers Road
Fiscal Year of award:	2017
Responsible Agency:	Berrien County Road Commission
MDOT Job Number:	12089
Project Limits:	0.3.miles East of Hollywood Road thence West 0.8 miles to Township Line
Project Length:	0.8 miles
Location:	Royalton Township
Work Type:	Resurface
Phase:	CON

Project Description: Resurface existing pavement that already has 4 ft wide shoulders



	Amount	Source
Federal	\$192,000	STP-Urban
State	-	-
Local	\$47,000	Berrien County
Total	\$239,000	

Activity	Estimated Date	Actual Date
Resolution of Support for Local Match Submitted to SMWPC		
Project Application Submitted to MOT		01/04/17
Grade Inspection Package Submitted to MDOT		01/04/17
Grade Inspection Meeting Scheduled		
Final Plan and Estimate to MDOT		
Project Obligated		
Project Letting	4/07/2017	4/07/2017
Construction Start	July 31	
Project Completion	09/02/17	09/02/2017

Project is: ☒ On Schedule ☐ Behind Schedule; Explain:

Low bid \$240,838.92



Southwest Michigan Planning Commission

376 West Main Street, Suite 130 • Benton Harbor, MI 49022-3651

Project Update Sheet

Project Name:	River Road
Fiscal Year of award:	2017
Responsible Agency:	Berrien County Road Commission
MDOT Job Number:	126674
Project Limits:	Over Pipestone Creek
Project Length:	
Location:	Sodus Township
Work Type:	Bridge replacement
Phase:	CON

Project Description: Replace the bridge over Pipestone Creek

	Amount	Source
Federal	\$864,000	BRT: STP-Bridge Replacement
State	\$162,000	M
Local	\$54,000	Berrien County
Total	\$1,080,000	

Activity	Estimated Date	Actual Date
Resolution of Support for Local Match Submitted to SMWPC		
Project Application Submitted to MOT		
Grade Inspection Package Submitted to MDOT		
Grade Inspection Meeting Scheduled		07/07/16
Final Plan and Estimate to MDOT		
Project Obligated		10/19/16
Project Letting	02/03/17	02/03/2017
Construction Start	4/17/2017	
Project Completion	09/15/17	

Project is: ☒ On Schedule ☐ Behind Schedule; Explain:

Date: 6/9/2017

Name: Tim Drews

Southwest Michigan Planning Commission

376 West Main Street, Suite 130 • Benton Harbor, MI 49022-3651

Project Update Sheet

Project Name:	Red Arrow Highway & John Beers Rod Intersection Improvements
Fiscal Year of award:	2017
Responsible Agency:	Village of Stevensville
MDOT Job Number:	130877
Project Limits:	400 ft. south of John Beers Rd to 400 ft. North of John Beers Rd.
Project Length:	.15 miles
Location:	Village of Stevensville
Work Type:	Restore and Rehabilitate
Phase:	CON

Project Description: Widening to add a center turn lane. Milling and Resurfacing. ADA sidewalk ramps, Traffic Signal modernization. Pavement markings and permanent traffic signs.

	Amount	Source
Federal	\$355,505	HSIP
State	\$0	-
Local	\$39,500	Village of Stevensville
Total	\$395,005	

Activity	Estimated Date	Actual Date
Resolution of Support for Local Match Submitted to SMWPC		
Project Application Submitted to MOT		8/11/2016
Grade Inspection Package Submitted to MDOT		8/11/2016
Grade Inspection Meeting Scheduled		9/2/2016
Final Plan and Estimate to MDOT		9/22/2016
Project Obligated		January 2017
Project Letting		3/3/2017
Construction Start	TBD	May 30
Project Completion	9/1/17	

Project is: ☒ On Schedule ☐ Behind Schedule; Explain:

Bids were received on March 3rd. The low bid was submitted by Severance Electric for \$372,189.15. Contractor is working through the MDOT contract process –Construction underway

Date: 6/9/2017

Name: Tim Drews

Southwest Michigan Planning Commission

376 West Main Street, Suite 130 • Benton Harbor, MI 49022-3651

Project Update Sheet

Project Name:	Colfax South Resurfacing
Fiscal Year of award:	2017
Responsible Agency:	City of Benton Harbor
MDOT Job Number:	130791
Project Limits:	May St. to Emery St.
Project Length:	0.25 mi
Location:	City of Benton Harbor
Work Type:	Resurface
Phase:	CON

Project Description: Full mill and fill with bike lanes. Partial AC of \$99,000 to be repaid on 2019
Additional funds added for sidewalk work

	Amount	Source
Federal	\$186,000	STP-Urban
State		
Local	\$96,700	City of Benton Harbor
Total	\$282,700	

Activity	Estimated Date	Actual Date
Resolution of Support for Local Match Submitted to SWMPC		
Project Application Submitted to MOT		4/7/2017
Grade Inspection Package Submitted to MDOT		4/7/2017
Grade Inspection Meeting Scheduled	5/1/2017	5/5/17
Final Plan and Estimate to MDOT	5/19/2017	5/19/2017
Project Obligated	July 2017	
Project Letting	8/04/2017	
Construction Start	September 2017	
Project Completion	November 2017	

Project is: ☒ On Schedule ☐ Behind Schedule; Explain:

Date: Click or tap to enter a date.
Name: Click or tap here to enter text.




Southwest Michigan Planning Commission

376 West Main Street, Suite 130 • Benton Harbor, MI 49022-3651

Project Update Sheet

Project Name:	Wallace Avenue
Fiscal Year of award:	2018
Responsible Agency:	City of St. Joseph
MDOT Job Number:	133290
Project Limits:	Lakeshore Drive to Lakeview Ave.
Project Length:	0.25 mi
Location:	City of St. Joseph
Work Type:	Reconstruct
Phase:	CON

Project Description: Full reconstruction of roadway with HMA or concrete pavement including curb and gutter, remove and replace ADA ramps as needed to meet current standards, install new storm sewer and sanitary sewer. Replace sidewalk, driveways as needed. This project is being undertaken as part of the City's ongoing combined sewer overflow (CSO) program and includes water main replacement.

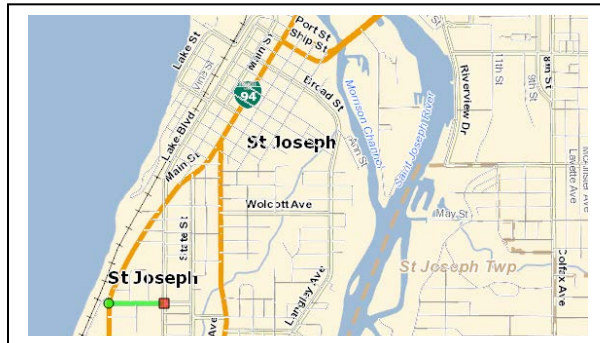

	Amount	Source
Federal	\$460,000	STP-Urban
State		
Local	\$1,000,000	
Total	\$1,460,000	

Activity	Estimated Date	Actual Date
Resolution of Support for Local Match Submitted to SWMPC	Complete	4/24/17
Project Application Submitted to MDOT	8/28/17	
Grade Inspection Package Submitted to MDOT	9/11/17	
Grade Inspection Meeting Scheduled	10/11/17	
Final Plan and Estimate to MDOT	11/17/17	
Project Obligated	December 2017	
Project Letting	2/2/18	
Construction Start	6/4/18	
Project Completion	9/21/18	

Project is: ☒ On Schedule ☐ Behind Schedule; Explain:

- Funding Resolution provided to SWMPC by email on April 28, 2017
- Anticipate issuing RFP for Engineering on May 19, 2017



Project Update Sheet

Project Name:	I-196 Overlay
Fiscal Year of award:	2017
Responsible Agency:	MDOT
MDOT Job Number:	118792
Project Limits:	I-94 to 0.5 miles South of M-63 (Exit 7)
Project Length:	8.09 miles
Work Type:	Restore & rehabilitate
Phase:	ROW

Project Description: Mill Existing & Multiple Course HMA Overlay

	Amount	Source
Federal	\$22,500	Interstate Maintenance
State	\$2,500	M
Total	\$25,000	

Project Status

Project is: ☒ On Schedule ☐ Behind Schedule

List what work has been done on this project to date:

Survey field work has been completed and is being analyzed. Geotech work will start soon. Project kickoff meeting was held 05/11/17 and minutes distributed. Will begin work on M-63 bridge alignments.



Project Update Sheet

Project Name:	M-139 Passing Flare
Fiscal Year of award:	2017
Responsible Agency:	MDOT
MDOT Job Number:	127448
Project Limits:	M-139 between Tanglewood and Anna.
Project Length:	0.71 miles
Work Type:	Traffic ops/safety
Phase:	ROW & PE

Project Description: Install passing flares

	Amount for ROW	Amount for PE	Source
Federal	\$4,093	\$53,096	CMAQ
State	\$907	\$11,774	M
Total	\$5,000	\$64,870	

Project Status

Project is: ☒ On Schedule ☐ Behind Schedule

List what work has been done on this project to date:

A consultant will be used to design this project. Traffic safety analysis has been requested.
Environmental classification is underway. Project will possibly move up to use FY 2019 funds to align with proposed M-139 mill and resurfacing project for 2019.



Project Update Sheet

Project Name:	M-63 Overlay
Fiscal Year of award:	2017
Responsible Agency:	MDOT
MDOT Job Number:	127563
Project Limits:	Winchester to I-94 BL
Project Length:	1.13 miles
Work Type:	Resurface
Phase:	CON

Project Description: Cold Milling and HMA One Course Overlay

	Amount	Source
Federal	\$80,525	STP – State Allocation
State	\$17,856	M
Total	\$98,381	

Project Status

Activity	Estimated Date	Actual Date
Project Application Submitted		
Grade Inspection Package Submitted		
Grade Inspection Meeting Scheduled		
Final Plan and Estimate		
Project Obligated		
Project Letting	04/07/2017	
Construction Start	06/15/2017	
Project Completion	08/15/2017	

Project is: ☒ On Schedule ☐ Behind Schedule; Explain:

Plans were turned in on 02/16/2017 for April Letting. Project came in 6.12% under the Engineers estimate.



Project Update Sheet

Project Name:	M-63 Crack Fill
Fiscal Year of award:	2017
Responsible Agency:	MDOT
MDOT Job Number:	128736
Project Limits:	I-94 to Midway Avenue
Project Length:	2.20 miles
Work Type:	Overband Crack Fill
Phase:	Construction

Project Description: Overband Crack Fill

	Amount	Source
Federal	\$ 28,412	STP – State Allocation
State	\$ 6,300	M
Total	\$ 34,712	

Project Status

Project is: ☒ On Schedule ☐ Behind Schedule

List what work has been done on this project to date:

Project has been turned in for the February letting. Bids came in 11.2% under Engineers Estimate. Construction to occur between May 17th and June 30th.



Southwest Michigan Planning Commission

376 West Main Street, Suite 130 • Benton Harbor, MI 49022-3651

Project Update Sheet

Project Name:	US-31 Longitudinal Joint Repair
Fiscal Year of award:	2017
Responsible Agency:	MDOT
MDOT Job Number:	128742
Project Limits:	Temp End Freeway to S JCT I-94
Project Length:	1.90 miles
Work Type:	Resurface
Phase:	CON

Project Description: HMA Longitudinal Joint Repair

	Amount	Source
Federal	\$234,036	National Highway System
State	\$51,897	M
Total	\$285,933	

Project Status

Activity	Estimated Date	Actual Date
Project Application Submitted		
Grade Inspection Package Submitted		
Grade Inspection Meeting Scheduled		
Final Plan and Estimate		
Project Obligated		
Project Letting	01/13/17	
Construction Start	06/26/17	
Project Completion	07/10/17	

Project is: ☒ On Schedule ☐ Behind Schedule; Explain:

Project was let and came in approximately 6% under. Construction will occur from June 26th to July 10th.



Project Update Sheet

Project Name:	EB I-94 Interchange
Fiscal Year of award:	2017
Responsible Agency:	MDOT
MDOT Job Number:	130008
Project Limits:	From Britain Avenue to I-196
Project Length:	3.87 mi
Location:	-
Work Type:	New route/structure (capacity increase)
Phase:	PE & SUB

Project Description: Reconstruction of I-94 and partial interchange.

	PE Amount	SUB Amount	Source
Federal	\$4,237,000	\$1,492,000	NH
State	\$940,000	\$331,000	M
Total	\$5,177,000	\$1,823,000	

Project is: ☒ On Schedule ☐ Behind Schedule

List what work has been accomplished to date for the PE Phase:

Preparing RFP to hire consultant to begin design work.

List what work has been accomplished to date for the SUB Phase:



Project Update Sheet

Project Name:	I-94 Road and Bridge Scoping
Fiscal Year of award:	2017
Responsible Agency:	MDOT
MDOT Job Number:	132824
Project Limits:	0.5 miles west of I94 BL(exit 23) to the St. Joseph River
Project Length:	3.50 miles
Work Type:	Miscellaneous
Phase:	EPE

Project Description: Scoping for Road and Bridge Work

	Amount	Source
Federal	\$0	—
State	\$400,000	M
Total	\$400,000	

Project Status

Project is: ☒ On Schedule ☐ Behind Schedule

List what work has been done on this project to date:

Geotech and bridge investigation have been completed. Progress meeting and bridge scoping progress meeting were held over the past week. Bridge fix selection meeting will be held 06/28/17.



Project Update Sheet

Project Name:	M-63 Bridge Replacement
Fiscal Year of award:	2018
Responsible Agency:	MDOT
MDOT Job Number:	115754
Project Limits:	On M-63 over I-196
Project Length:	-
Location:	-
Work Type:	Bridge Replacement
Phase:	CON

Project Description: Bridge Replacement

	Amount	Source
Federal	\$4,136,000	BRI
State	\$460,000	M
Total	\$4,595,000	

Activity	Estimated Date	Actual Date
Resolution of Support for Local Match Submitted to SWMPC		
Project Application Submitted to MOT		
Grade Inspection Package Submitted to MDOT		
Grade Inspection Meeting Scheduled		
Final Plan and Estimate to MDOT		
Project Obligated		
Project Letting		
Construction Start		
Project Completion		

Project is: ☒ On Schedule ☐ Behind Schedule; Explain:

FTC&H will be determining the appropriate alignment to use for the bridge. Bridge design will begin thereafter.



Project Update Sheet

Project Name:	I-196 Overlay
Fiscal Year of award:	2018
Responsible Agency:	MDOT
MDOT Job Number:	118792
Project Limits:	I-94 to 0.50 miles South of M-63 (Exit 7)
Project Length:	8.09 mi
Location:	-
Work Type:	Restore & Rehabilitate
Phase:	CON

Project Description: Mill Existing & Multiple Course HMA Overlay

	Amount	Source
Federal	\$15,840,000	IM
State	\$1,760,000	M
Total	\$17,600,000	

Activity	Estimated Date	Actual Date
Resolution of Support for Local Match Submitted to SWMPC		
Project Application Submitted to MOT		
Grade Inspection Package Submitted to MDOT		
Grade Inspection Meeting Scheduled		
Final Plan and Estimate to MDOT		
Project Obligated		
Project Letting		
Construction Start		
Project Completion		

Project is: ☒ On Schedule ☐ Behind Schedule; Explain:

Survey field work has been completed and is being analyzed. Geotech work will start soon. Project kickoff meeting was held 05/11/17 and minutes distributed. Will begin work on M-63 bridge alignments.



Project Update Sheet

Project Name:	I-94 WB Overlay
Fiscal Year of award:	2018
Responsible Agency:	MDOT
MDOT Job Number:	128907
Project Limits:	East of I-196 to West of M-140
Project Length:	5.60 mi
Location:	-
Work Type:	Resurface
Phase:	PE

Project Description: Repair Existing & Multiple Course HMA Overlay

	Amount	Source
Federal	\$1,197,000	IM
State	\$133,000	M
Total	\$1,330,000	

Activity	Estimated Date	Actual Date
Resolution of Support for Local Match Submitted to SWMPC		
Project Application Submitted to MOT		
Grade Inspection Package Submitted to MDOT	01/15/2019	
Grade Inspection Meeting Scheduled		
Final Plan and Estimate to MDOT	06/03/2019	
Project Obligated	11/18/2019	
Project Letting	01/10/2020	
Construction Start	04/01/2020	
Project Completion		

Project is: ☒ On Schedule ☐ Behind Schedule; Explain:

PE Phase will be obligated on 08/01/2017.



700 Broad Street • St. Joseph, Michigan 49085-1276 • www.sjcity.com

DEPARTMENTS

ASSESSOR
269-983-1231

ATTORNEY
269-983-5541

CLERK
269-983-6325

COMMUNICATIONS
& MARKETING
269-983-0349

ENGINEER
269-983-5541

FINANCE/TREASURER
269-983-4731

HOWARD ICE ARENA
269-985-8795

INSPECTIONS &
CODE ENFORCEMENT
269-983-1212

MANAGER
269-983-5541

PERSONNEL
269-983-0443

PLANNING & ZONING
269-983-1212

PUBLIC SAFETY:
EMERGENCY 9-1-1

DISPATCHER
269-983-3060

POLICE
ADMINISTRATION
269-985-0300

FIRE
ADMINISTRATION
269-983-4641

PUBLIC WORKS:

PARKS & CEMETERY
STREETS & SANITATION
269-983-6341

WATER/SEWER BILLING
269-983-6324

WATER TREATMENT
PLANT
269-983-1240

WEST BASIN MARINA
269-983-5432

June 9, 2017

Mr. Brandon Kovnat
Associate Transportation Planner
Southwest Michigan Planning Commission
376 West Main Street
Suite 130
Benton Harbor, MI 49022

RE: TIP Amendment Request – Wallace Avenue Project

Dear Mr. Kovnat:

I am writing to you in follow up to the email sent on June 8, 2017. The City of St. Joseph is requesting a TIP amendment to extend the limits of the Wallace Avenue Project. The City desires the change because we have identified a sanitary sewer pipe run that is in poor condition immediately to the east of the project limits. A snapshot of the sewer Pipeline Assessment Certification Program (PACP) rating map is attached. Additional project details follow.

Project Name: Wallace Avenue
Original Project Limits: Wallace Avenue – Lakeshore Drive to Lakeview Avenue (0.25 mi)
Fiscal Year of Award: 2018
MDOT Job Number: 133290
Amended Limits: Wallace Avenue – Lakeshore Drive to South State Street (0.37 mi)
Local Funding: Approximately \$1,000,000
Federal Funding: \$460,000 STP-Urban (**No change to federal funding requested**)
Brief explanation for amendment requested: Stated above and in the attached email.
Date of Request: June 9, 2017

Please feel free to contact me if you have and questions or need additional information.

Sincerely,

Tim Zebell, P.E.
City Engineer

Cc: Kim Gallagher, Senior Planner, Southwest Michigan Planning Commission
John Hodgson, City Manager
Sara McCallum, Finance Director/City Clerk
Tom MacDonald, Director of Public Works

FY 2017-2020 Berrien County CMAQ Project List
Approved at the January 26, 2017 Berrien County CMAQ Meeting

Agency Name	Project Name	Federal Amount	Non-Federal Amount
2017 Target		\$598,254	
TCATA	Four (4) New Buses	\$230,000	\$57,500
Berrien Bus	Five (5) New Buss	\$356,254	\$89,064
SWMPC	Rideshare	\$12,000	\$0
2017 Total		\$598,254	
Balance		\$0	

2018 Target		\$598,254	
SWMPC	Rideshare	\$12,000	\$0
Benton Harbor	Traffic Signal Replacement for Pipestone at Jefferson St	\$264,254	\$0
Berrien Bus	1 New Van	\$42,000	\$10,500
Berrien Bus	5 New Buses	\$280,000	\$70,000
2018 Total		598,254	
Balance		\$0	

2019 Target		\$598,254	
Berrien County Road Commission	S Roosevelt Road over Hickory Creek Non-Motorized Path	\$398,254	\$176,746
SWMPC	Rideshare AC	\$12,000 (AC)	\$0
Berrien Bus	Three New Buses	\$200,000	Unknown
2019 Total		\$598,254	
Balance		\$0	

2020 Target		\$598,254	
SWMPC	Rideshare	\$12,000	\$0
SWMPC	Rideshare ACC	\$12,000	\$0
Berrien County Road Commission	Traffic Signal Replacement on Napier Avenue at Leeds Avenue	\$240,000	\$0
Berrien Bus	2 New Buses	\$120,000	\$30,000
TCATA	3 New Buses	\$210,000	\$35,000
2020 Total		\$594,000	
Balance		\$4,254	

Illustrative List			
Buchanan	Traffic Signal Replacement for Red Bud Trail at River St	\$240,000	\$0
Benton Harbor	Traffic Signal Replacement for Pipestone at Market St	\$240,000	\$0
TCATA or Berrien Bus	Bike Racks for Buses	\$2,500-\$5,00 apiece	
